

Monthly Projects Update – October 2022

Bay Road

- Stage 3, line marking of sealed road and shared path sections has been completed including signage installation.
- Stage 2 works behind the kerb, including backfilling, placing crusher fines and shared path construction are well underway.
- Extending residential stormwater overflow outlets to the road or collection basins are being installed where required.
- Main stormwater line and extensions are now complete. Final walkover and CME demobilisation to occur late September.
- All machine laid kerb and tie-inns are now complete. Pram ramps to be completed late September ready to hand over site completely to Downer.
- Electrical conduits and water meter connections are being installed continuously under Bay Road to ensure the new road surface is not disturbed once completed.



Sinkhole


- Backfilling of the sinkhole and the over excavated area is complete.
- Compaction testing undertaken on the road pavement level passed, and the road was deemed safe to open.
- Temporary fencing and signage were removed, speed restrictions remain in place until the road can be resealed.
- Resealing due to be undertaking late September early October, weather permitting.

George Street Stormwater Upgrade

- Installation of stormwater infrastructure in Zone 1, intersection of Henry and George Street, is completed. Trenches have been reinstated, asphalt laid and intersection re-opened.
- Conflicting services in this intersection required a design change; on-site adjustments were necessary to suit and keep the project on schedule.
- This included constructing an in-situ junction box and modifications to new side entry pits and junction boxes.
- Contractor has moved south, commencing works in the second zone. Zone 2 works are going well despite some rock and groundwater being present.

Monthly Projects Update – October 2022

- Zone 2 works set to be completed before the long weekend and school holidays where site works will halt for the entirety of the school holidays. Asphaltting of trench, removal of machines, barrier fencing and road cleaning to occur before the road is re-opened to public traffic.
- Contractor and Council staff continue to liaise with business owners to keep them updated of the projects progress and inconveniences.

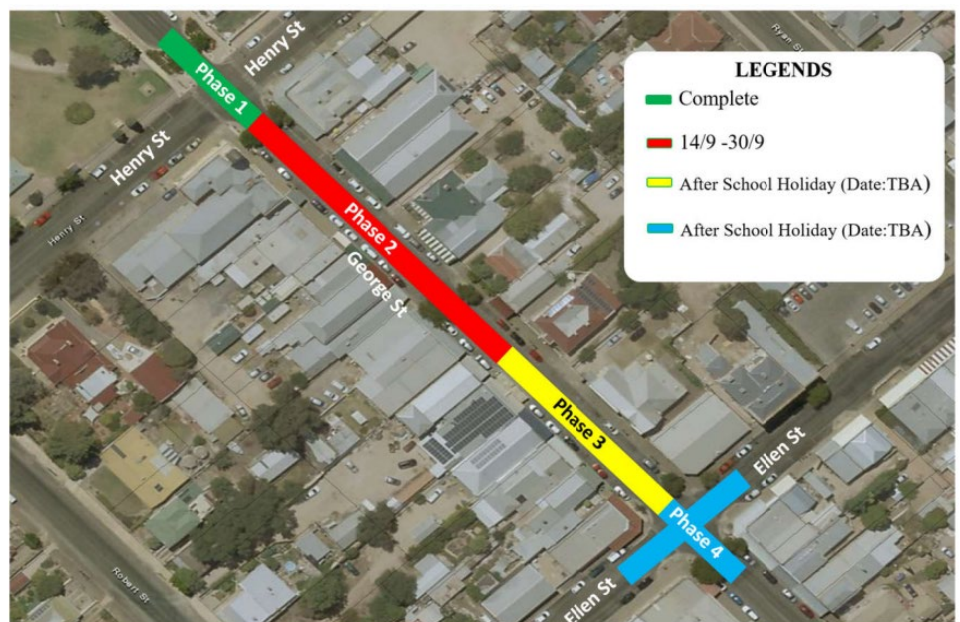

Hedonbar

- Construction works are well underway. Council staff have constructed the timber frames for the toilet block.
- Plumbers and electricians have first fixed the power, water and drainage to the new toilet block.
- Contractors are completing the plasterboard to the toilet, and flooring contractors are scheduled late September, before Council staff can begin second fix carpentry.
- Stage 1 of the power separation has been completed and new LED lighting has been installed in the shed for both Hedonbar and the National Trust.
- Contractors have completed the dividing wall between Hedonbar and the National Trust.

Monthly Projects Update – October 2022

- Their focus now is on the modifications to the Western side of the shed. These include the removal and infilling of two large sliding doors for Hedonbar and creating a sliding door opening for the National Trust.



Wallaroo to Moonta shared path

- The Contractor has commenced excavation works on the shared path from Ryan Street to Park Terrace, Wallaroo.
- Sections of the path from Ryan Street to Cornish Terrace have been concreted and are complete, weather is making these works challenging.
- Approximately 1,060 meters of shared path to be completed in the Wallaroo section.
- Separate contractors have been working on the section of shared path between Mines Road and the Moonta Information Centre running through the National Trust Precinct.
- Approximately 250 meters of shared path to be laid at the Moonta end to link the path together.
- Sealing of this section of the path will be scheduled in for the warmer months.



Monthly Projects Update – October 2022

Unsealed Roads – Patrol Grading

Beare Road, Wintinerta Road, Blackoak Road, Pine Forrest Road, Leavre Road, Larwood Road, Willamulka Road, Old Well Road, Thrington Hill Road, McKay Road, Haynes Road, West Ella Road, Paskeville Road, Kuchel Road, New Holland Road, Stoney Ridge Road, Pontifex Road, Harrop Road, Bowey Road.

Infrastructure Records Management

Records are a combination of Customer Service Requests (CSRs), emails, letters and works (Before You Dig requests, Applications to undertake works on Council Land and Land Access and Activity Notices etc.)

For the month of August 2022, the Infrastructure Department received 570 records:

