<u>Bay Road</u>

- Works began back on-site 10th January focusing on kerb preparation and laying from Coast Road to Hughes Avenue.
- Stormwater installation is nearing completion in Stage 1 (Caroline Street to Haylock Road).
- Kerb preparation and laying to proceed the completion of these works.
- Council contractors continuing to install conduits for power and water for future proofing.
- Downer set to mobilise to site mid to late February to begin road reconstruction works of completed stages 1 & 3.
- CME to continue stormwater installation through stage 2.


Cemetery walls - Moonta

- The contractors have made good progress to the inner N/E wall. As you can see, the old practice of using cement base render for repair work has eroded the very bowels of the wall.
- Some areas have required extensive restoration work. The contractors have had to battle the hot weather and also COVID-19 restrictions. As per the photos, the walls are looking great.
- They still have some challenging areas, but things are tracking well.



YP Alliance - Roadworks

- Shoulder widening works on the Agery Road and Arthurton Road project commenced on Monday, 24th January.
- This project is part of an alliance with Barunga West and the Yorke Peninsula Councils where funding was sought through the Local Government Infrastructure Partnership Program (LGIPP).
- Works include the topping up of material on the roads shoulder, compacting, spray sealing additional shoulder width and line marking.
- Copper Coast's portion of the project is scheduled to take around a month, with works starting in Moonta, Verran Terrace/Arthurton Road.
- Agery-Cunliffe road length is 13.1km and Verran-Arthurton is 6.3km long.

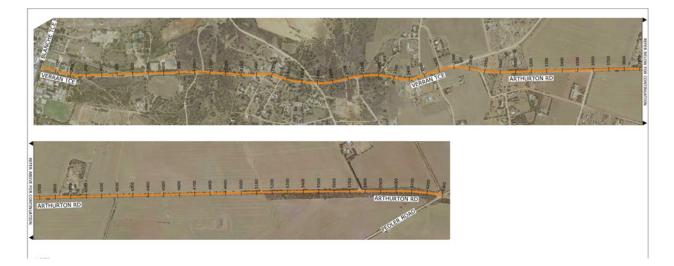

<u>Moonta Dog Park</u>

• The Moonta Dog Park is nearing completion and is scheduled to open within February. This is to allow the lawn enough time to establish to protect against the imminent inundation of furry paws.



Kadina Lagoons

- Lagoon 1 dewatering completed over the Christmas period and allowed time for evaporation to assist in drying the sludge.
- Earthworks have commenced with the removal of Bio-Solids (sludge) and excess clay liner approximately 10,000m3.
- Liner forecast to be installed mid-March.
- These works are required as part of the Environmental Improvement Plan (EIP) that has been put in place by the EPA.





Otago Road - Sand Drift Implementation

- Prior to Christmas, wheat straw was spread over the dune system to help stabilise the sand dune system and reduce the movement of sand from seasonal on-shore winds.
- Local produce and contractors were sourced to assist in the spreading.
- The straw is to also act as much needed source of mulch required for 10,000 seedlings that have been ordered ready for the planting season of April/May.
- Council staff have been working the consultants and their recommendations in the continuing effort to reduce the effects of the sand movements.



Unsealed Roads – Patrol Grading

Old Wallaroo Road, Warburto Road, Martin Terrace, Hazelgrove Road, Busshenschutt Road, Fairfield Road, Rosslyn Road, Hamley Hill Road, Cowling Terrace, Hills Road, Shields Road, Heyward Road, Heath Road, Magazine Road, Thomson Street, Musgrave Terrace, East Terrace, Wallaroo/Tickera Road, Jones Road, Point Riley Road, Rees Road, Kinnear Road, Kadina/Tickera Road, Beare Road, Angove Lane, Pedler Lane, Osborn Lane, Stock Road, Giesecke Road, Hare Terrace, Prout Road, Chapman Road, Binney Road, Cavanagh Road, Bird Island Road, Ellis Road, Betts Road, Harbison Road, Lehman Road, Chatties Lane, Hopgood Road, Myponie Point Road, Black Rock Road, Cross Road, Adams Plain Road.
