Moonta Road, Moonta Stormwater Upgrade

- The majority of the project has been completed, with contractor MA Skinner having demobilised from site.
- Their recent works have seen
 - o all culverts under Coast Road, Carlisle Street and East Terrace installed
 - o drain excavation, shaping and bund wall construction completed
 - o rock scouring and rock edge wall lining completed
- Contractor encountered a large amount of rock being within a section of the swale drain, despite this delays were kept to a minimum.
- Fencing, bridge and vegetation that was removed as part of the upgrade, will be reinstated as the next, and final stage of this project.





PLEC Stage 2 – Undergrounding of power lines

- Council and contractor working with SA Power Networks to underground power. Stage 2 is from Tossell Street down to the end of Bay Road, Moonta Bay.
- Stage 1 from corner of George Street/Bay Road to past Caroline Street to commence soon.
- Stage 2 includes an upgrade to the Transformer that feeds into the Moonta Bay Caravan Park.
- Conduits have been installed under Bay Road prior to road stabilisation so Bay Road won't be dug up.
- Expected time of Stage 1 and 2 completion June/July 2023.





Polgreen Park – Public Toilet Upgrade

- Timber frame construction work on the new toilet has been completed since the laying of the concrete slab.
- Council staff have been working on the installation of the external cladding getting the toilet to lock up
- Plumbing and electrical contractors are scheduled to install their respective first fix items before internal cladding can commence.
- Painting contractor has completed painting external exposed timber members.





Unsealed Roads 5 Year Re-sheet Program

- Contractor currently working on Allen Road, Kadina.
- 4km of vegetation has been cleared along the verge.
- 1,100m subgrade formed up to compacted to finished level ready for final 150mm PM2 layer of rubble.
- Council construction crew working on Koch/Whites Road, Kadina.
- 900m subgrade formed up to finished level ready for final 150mm PM2 layer.
- Contractor working Thomas Plains Road.
- Final 1km subgrade formed up to compacted to finished level ready for final 150mm PM2 layer of rubble.





Moonta Bay Revetment Wall & Beach Access

- Council construction crew have completed reforming 96m of the revetment wall, consisting of 50mm to 100mm ballast rock, covered in R900 Texcel Geofabrics, finished off with large 1m rocks.
- 39 metres is prepared with ballast rock, council currently sourcing large rock to finish of this section.
- 30 metres still required to be constructed to finalize the revetment wall up to the Moonta bay access ramp.
- Access ramp design and supply tender was awarded and the material is in production. Access ramp is to be a fibreglass reinforced product in lieu of a timber framed construction.





Kadina Lagoons


- Contractor has completed the HDPE (High Density Polyethylene) lining of lagoon 1A
- Final inspection and Sign off completed by WGA (Wallbridge, Gilbert and Aztec) engineering
- Waiting approval from the EPA and Department of Health to commence filling.
- Once approved, closes out Action 8 of the EPA Environmental improvement plan.





Auslan Signage

- To further enhance accessibility within our region, Council staff will be installing 3 signs featuring Auslan signage at South Beach, Port Hughes, Wallaroo Adventure Playground and Victoria Square, Kadina playgrounds.
- This initiative assists in learning Auslan sign language and interacting with Deaf and Hard of Hearing kids within our community.

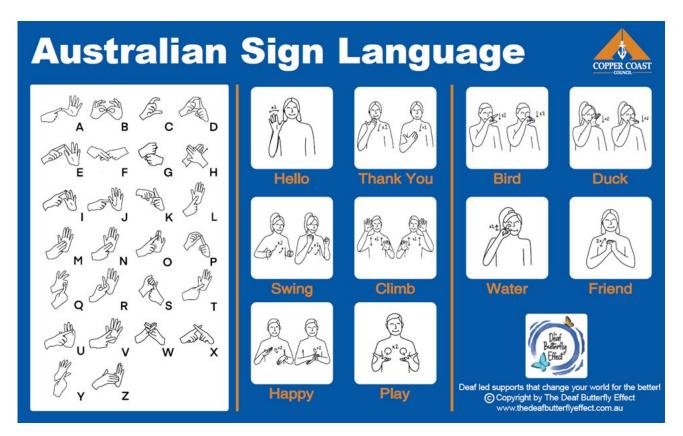

Unsealed Roads

Bussenschutt Road, Daddow Road, Mitchell Road, Rodda Road, Schilling Road, White Road, Koch Road, Cunliffe/Moonta Road, Sandercock Road, Allen Road, Mill Road, Sterle Road, Parker Road, Cavanagh Road, Stock Road, McCauley Road, Martinga Road, Haynes Road, Milne Road, Daly Street, Smith Avenue, Young Road, Sterling Road, Rosewarnes Road, Drain Road, Creswell Road, Matta Road, Davison Road, Morphett Road, Datsun Road, Barkley Road, Robinson Road, Franklin Road, Walter Road, Duncan Road, Copper Lane, Fyfe Road, Magazine Road, Racecourse Road, Musgrave Terrace, Hawke Road, Field Road, Anthony Terrace, Piper Street, David Street, Brittain Road, Harris Road, Dunn Road, Donaldson Road, Ellis Road, Rosslyn Road, Bulls Road, Heath Road Martin Terrace, Helston Road, Fairfield Road, Leaver Road, Blackley Road, Haselgrove Road, Manual Road, Old Wallaroo Road, Crutchett Road, Beare Road, Jacka Lane, Collins Road, Shepherdson Road, Prisk Lane, Newland Road, Waterhouse Road, Karkarilla Road, Prout Road, Lancelot Road, Ryan Road, Retallick Road, Wedge Road, Morphett Road, Polgreen Road, Lambert Road, Goldsworthy Road, Tank Road, Rossiters Road, Warmington Road, Creswell Terrace, Browning Road, Derrington Terrace, Downer Road, Duncan Road, Truer Street, Marshall Road, Morcombe Road, Warren Road, Hare Terrace, Tonkin Road, Osborne Lane, Angove Lane, Appleton Road, Coast Road, Giesecke Road, Binney Road, Hills Road, Chapman Road.

Infrastructure Records Management

Records are a combination of Customer Service Requests (CSRs), emails, letters and works (Before You Dig requests, Applications to undertake works on Council Land and Land Access and Activity Notices etc.).

For the month of March 2023, the Infrastructure Department received 514 records:

