

Monthly Projects Update – May 2022

Copper Coast Sports and Leisure Centre

- Following a recent Elected Member walk-through, the bathrooms have now been finished.
- The stage doors and corridor door have been replaced with approved fire rated doors, these will be correctly tagged and certified. There is still a wait for the fire doors that will replace the roller doors on Court 2.
- The flooring is the next focus area which is expected to take place in May 2022.



Kadina Lagoons

- Kadina lagoon 1B earthworks are nearing completion.
- Additional balance pipe work and control pits have been installed.
- 1B liner scheduled to be installed mid-May 2022.
- Earthworks on lagoon 1A scheduled to commence mid-May 2022.



Wallaroo and Moonta Shared Path

- The rubble sub-base has been completed from Coota Road though to Cavanagh Road.
- Sealing of the first section has been rescheduled to commence mid-May 2022. Sealing contractor has been affected by COVID-19, severely hindering their operations.



Monthly Projects Update – May 2022

Bay Road

- Stage 1 kerb and channel is nearing completion, this will complete CME's scope of works for Stage 1, allowing Downer to take over the site in this stage.
- Stormwater works continuing along the main line of Stage 2, rock and groundwater is still being reported in this zone.
- Stage 3 kerb and channel is very close to completion (Highview Grove to Coast Road) – minor kerbing tie-ins to be completed.
- SA Water have provided a solution to service clashes on Coast Road/Bay Road intersection. SA Water have engaged contractors with works on the main relay expected to begin in May 2022.
- Downer have commenced work in Stage 3, focusing on backfilling and shaping behind the kerb and also preparing the new shared path. These works will allow for better access to the property owners and pedestrians.
- Stabilisation of road (Highview Grove to Coast Road) expected to commence at the end of May 2022.



Bews Square Upgrade

- The upgrade to Bews Square has started with paving works surrounding the monument.
- Works will also include reshaping the mounds, installing retaining walls and increasing the vegetation to further enhance this underutilised open space.



Monthly Projects Update – May 2022


Cemetery Walls - Moonta

- Work is progressing well on the outer north/north east wall with the outer north east wall nearing completion.
- Portions of the wall have required rebuilding due to incorrect cement render being used.
- Once this wall has been completed, the contractors will commence on the northern wall.



Queen Square Upgrade

- Demolition of all existing fixtures, ceilings, concrete paths and external brick wing walls has been completed.
- Focus is now on rendering the existing internal and external walls to allow for an alternate clean and modern finish.
- New timber fascias, colorbond gutters and roofing are in progress. To complete the building upgrade, a new epoxy floor covering is to be laid and finished with new partitions and fixtures.
- The toilet upgrade is expected to be complete by the end of June 2022, there are new shared paths to be installed throughout the park and around the toilet that will proceed the completion of this project.

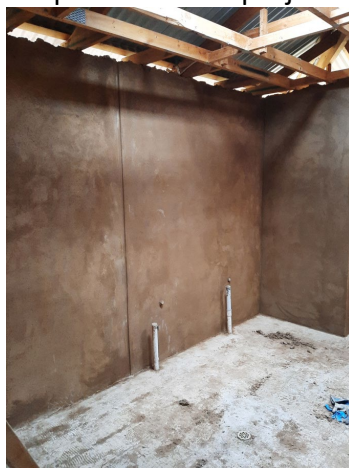

Monthly Projects Update – May 2022

Wallaroo Entrance Road

- Beare Street to Athena Drive Stage 1 has been completed. This included the first layer of hotmix seal for this segment of road.
- Road was left 50mm below final finish level to allow Council to install kerbing and channel.
- Survey of site has recently been completed and provided to Tonkin Consulting to progress construction documents. This design will include; carparking, stormwater infrastructure assessments, kerb and channel and final road design levels.
- Road is currently maintained by Department Infrastructure Transport (DIT) who are funding the main carriageway (road) and Council's responsibility is the stormwater and kerbing.
- Council are continuing to work in close partnership with DIT.



Unsealed Roads – Patrol Grading

Retallick Road, Wedge Road, Morphett Road, Polgreen Road, Lambert Road, Goldsworthy Road, Fisher Road, Appleton Road, Coast Road, Giesecke Road, Binney Road, Hills Road, Chapman Road, Osborn Lane, Angove Lane, Deeble Street, Jacka Lane, Martin Terrace, Harris Lane, Hopgood Road, Rees Road, Black Rock Road, Myponie Point Drive, Kinnear Road, Cross Road Point Riley Road, Wallaroo/Tickera Road, Jones Road, Chatties Lane, Hopgood Road, Adams Plain Road, Kadina/Tickera Road, Rossiters Road, Chapman Road, Blackoak Road, Beare Road, Leavre Road, Pine Forrest Road, Old Well Road, Thrington Road, Wintinerta Road, Thomas Plains Road, McKay Road, Haynes Road, West Ella Road, Paskeville Road, New Holland Road, Stoney Ridge Road, Kuchel Road, Pontifex Road, Harrop Road, Bussenschutt Road.
