

## Monthly Projects Update – August 2022

### Bay Road

- Downer have finalised works behind the kerb in stages 1 & 3, the shared path in these zones is ready for sealing.
- The additional 90-degree Car Park extension near Tossell Street is completed and ready for sealing.
- Downer's civil contractor has completed road cut and fills to stage 1 and stage 3
- Downer has mobilised the stabilisation crew to site and have begun work in stage 3.
- Stormwater installation works are continuing on the main line and have progressed past Bartlett Street intersection. There is approximately only **100m** remaining with completion of the main stormwater line programmed by the end of July.
- Kerbing preparation and laying is proceeding this, the concrete contractors have progressed well over the past month.
- CME's contracted works are nearing completion, some minor storm water branch lines and kerbing preparation and laying in stage 2 is all that remains.



### Wallaroo to Moonta shared path

- Shared path sub base is completed from Coota Road to Magazine Road, ready for spray seal. This completes the entire length from Magazine Road, Wallaroo to Mines Road, Moonta.
- Contractors are scheduled to commence the section between Mays crossing to Park Terrace in August.
- Separate contractors are working with Council to complete the section from Mines Road to the Moonta Information Centre.
- Signage, bollards, line marking etc. will proceed the final sealing of the track to allow for this section to be utilised whilst the other zones are being completed.

### Road Reseal Program

- Council are waiting for contractors to return to continue work on road reseal program and final sealing of Moonta to Wallaroo bike path.
- Sealing expected to happen late July/early August.

## Monthly Projects Update – August 2022

### Agery Road- Roach Street Kadina

- Kerb preparation and replacement on both sides is now complete and backfilled.
- Kerbing works on Agery Road is completed, including the introduction of a spoon drain at the Mines Road intersection to assist with stormwater flows.
- All side entry pits on Roach Street and the addition of an extra one at the intersection of Agery and Roach have been raised and repaired to assist in stormwater run-off.
- Council staff and the contractor are liaising with SA Water to lower property connections to allow the safe operation of the stabilisation machine throughout Agery Road.
- Intersection remediation works are underway, this will eliminate an existing spoon drain and remove the depression in the road.
- Once completed both Agery Road (Mines to Roach) and Roach Street (Copper Coast Highway to Agery Road) will have a hotmix 40mm seal.



### Kadina Lagoons

- Lagoon 1B liner installation completed, final engineering inspection has been completed and passed.
- Balance pipe from lagoon 1B to lagoon 2 to install.
- Continuous ground monitoring scheduled for the next 6 months.
- Works on Lagoon 1A will commence towards the end of August





## Monthly Projects Update – August 2022

### Bews Square Upgrade

- Both sections of garden beds, Bews and the Lighthouse, have been planted out and mulched.
- Bews lawn area has had top soil spread and is awaiting SAPN to provide a power supply for the irrigation to become live. Once this has been undertaken, the soil will be seeded.
- Lighthouse area lawn section is waiting for SA Water to install a meter. Once this has been undertaken, the soil will be spread and seeded.
- Seating has been installed into the newly created sitting area of Bews Square and concrete garden edging has been installed to the lighthouse garden beds.



### Queen Square Upgrade

- The final touches were finished off, fences were removed and the toilets were open for business on the 14<sup>th</sup> July 2022 at 2pm.
- Final touches included;
  - Installation of toilet partitions and sanitary items,
  - Painting
  - Installation and completion of all electrical and plumbing requirements
  - Concrete pathways
- Council's Building Staff were able to introduce different products and challenge existing methodologies used on previous builds that will improve Council's amenities into the future.



## Monthly Projects Update – August 2022



### Cemetery Walls - Moonta

- Contractors have been up against it with the weather and larger holes due to cement mortar wash out.
- There is an estimated 2 weeks remaining on the outer Northern wall before works can start on the inner wall.
- With minimum weather delays, completion is approximately 6 to 8 weeks away.



### Infrastructure Records Management

Records are a combination of Customer Service Requests (CSRs), emails, letters and works (Dial Before You Dig requests, Applications to undertake works on Council Land and Land Access and Activity Notices etc.). For the month of June 2022, the Infrastructure Department received 492 records:

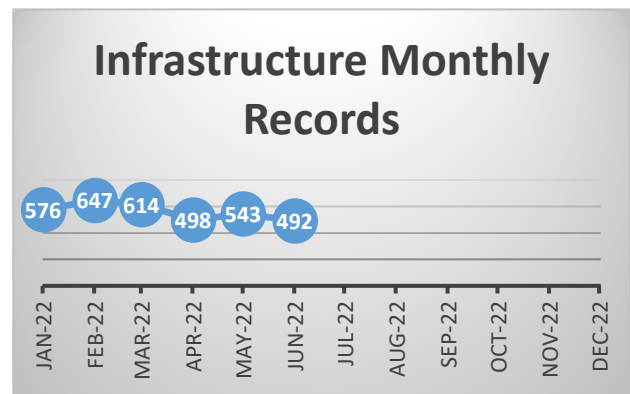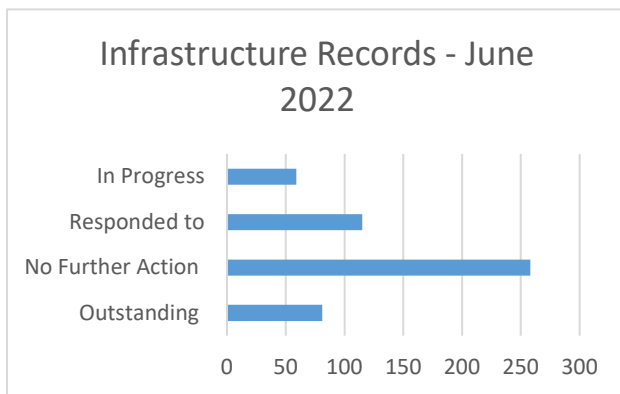

### Unsealed Roads – Patrol Grading

Adams Plain Road, Kadina/Tickera Road, Black Oak Road, Beare Road, Old Wallaroo Road, Harbison Road, Wall Road, Lehmann Road, Thompson Road, Cornish Terrace, Banks Road, Willamulka Road, Pine Forrest Road, Leavre Road, Thomas Plain Road, McKay Road, Haynes Road, West Ella Road, Paskeville Road, New Holland Road, Kuchell Road, Stoney Ridge Road, Pontifex Road, Harrop Road, Bowey Road, Drewitt Road, Bussenschutt Road, Green Plains Road, Stenning Road, Reid Road, Rodda Road, Copper Hill Road.
