

Monthly Projects Update – April 2021

Bay Road

- Five information sessions have been held at the Moonta Town Hall with residents and community groups.
- Contact has been made with the project management team from Tonkin Consulting.
- Site establishment works have begun on Majors Road.
- Works are set to begin on Bay Road in April.

Frances Terrace

- Stage 5 (Roundabout) Civil Works completed.
- Underground storm water, SEP's, pram ramps and curbing and asphalt complete.
- Underground lighting works and conduit laying complete, including laying of blind conduits for future undergrounding of overhead powerlines.
- Road and shared path pavement base preparation and deep lift asphalt completed.
- Temporary line marking and bollards installed prior to Easter to allow for the road opening.



Monthly Projects Update – April 2021


Cemetery

- The Moonta cemetery wall repairs are progressing well.
- The stonemasons have colour matched the mortar mix to the original wall.
- The wall, in some areas, is in poor condition due to the structure being compromised by tree roots and moisture.



Pedestrian Crossing - George Street


- Moonta's George Street wombat crossing, and left in, left out only, of the Drakes complex is to be constructed as per the adopted Moonta Master Plan.
- The plan depicts additional raised verges and garden beds on either side of the road.
- Consultation with the businesses and owners has begun.
- Construction will commence after the April school holidays and may include night works.

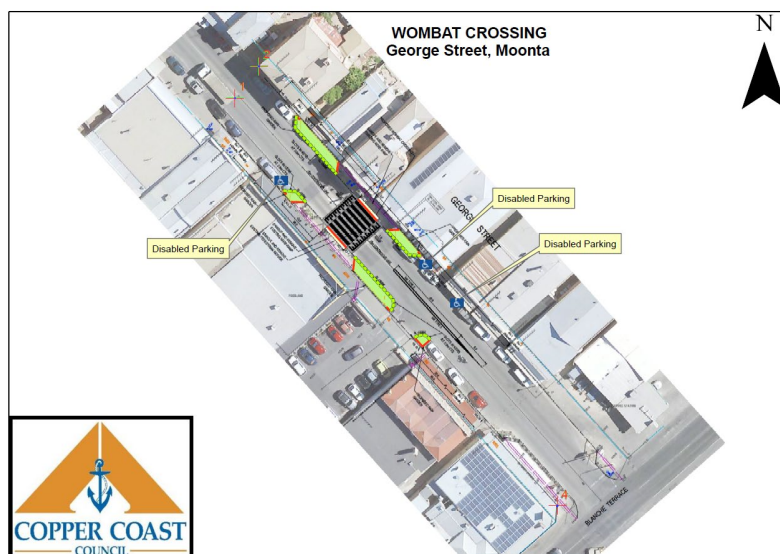

Monthly Projects Update – April 2021

Ellen Street carpark

- Current in and out access on Ellen Street to become an entrance only.
- A heritage mural will be painted on the wall, design TBC.
- Cobblestone paved paths will be used to give the public access to amenities and carpark.
- Additional timber screening to be utilised near amenities building and electrical box.
- Access to be increased with additional pram ramps planned.
- Raised concrete garden beds to be installed to identify vehicle access and stopping points.
- Works will commence Tuesday, 6 April 2021.

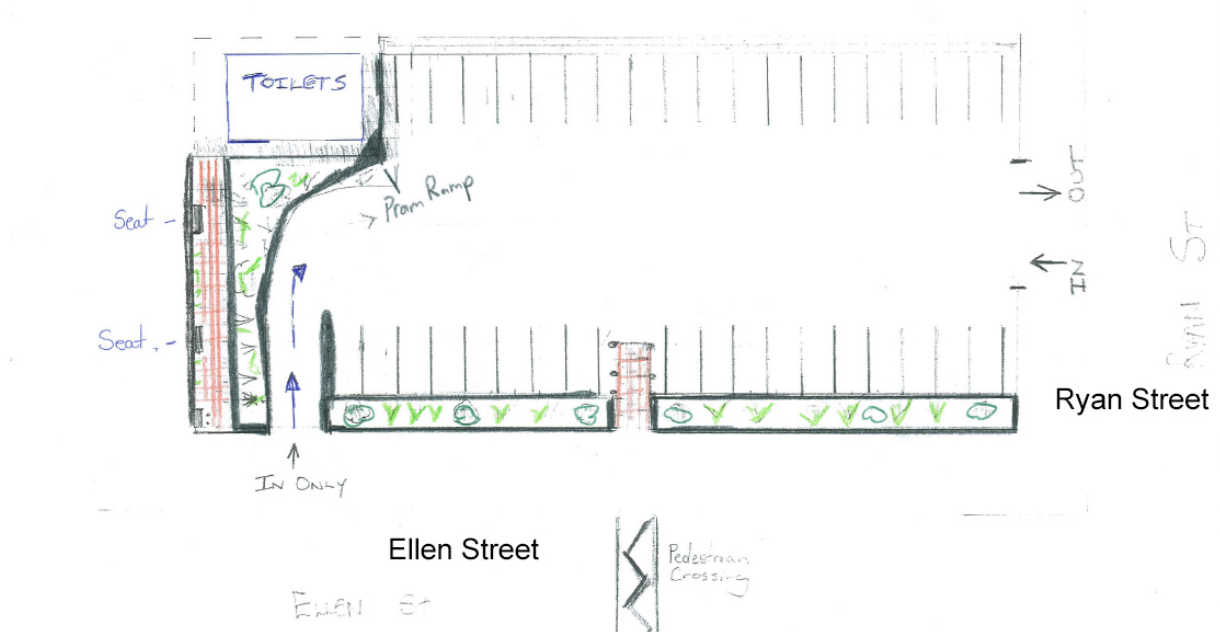

Unsealed Roads

Rosewarne Road, Daly Road, Duncan Road, Smith Avenue, Matta Road, Davidson Road, Young Street, Copper Hill Road, Paskeville Road, Bussenschutt Road, Daddow Road, Schilling Road, Mitchell Road, Koch Road, Redding Road, Allen Road, Mill Road, Woodward Road, White Road, Moonta/Cunliffe Road, Sandercock Road, Sterle Road, Parker Road, David Street, Brittain Road, Haynes Road, Drain Road, Donaldson Road, Ellis Road, Dunn Road, Roslyn Road, Bulls Road, Heath Road, Martinga Road, Milne Road, Racecourse Road, Morphett Road, Anthony Road, Field Road, Datson Road, Sterling Road, Musgrave Terrace, Federal Avenue, Devon Road, Hawke Road, Robinson Road, Barkla Road, Austin Road, Fyfe Road, Walter Road, Franklin Road, Martin Terrace, Helston Road, Fairfield Road, Haselgrove Road, Old Wallaroo Road, Bird Island Road, Warburto Road, Dayman Road, Hayward Road, Coota Road, Sandercock Road, Shepherdson Road, Collins Road, Retallick Road, Tank Road, Rossiters Road, Fisher Road, Cavanagh Road, McCauley Road, Newland Terrace, Waterhouse Street, Karkarilla Road, Truer Street, Morcombe Road, Ryan Road, Warmington Road, Browning Road, Creswell Terrace, Daly Road, Derrington Terrace, Duncan Road, Deeble Road, Osborne Lane, Chapman Road, Crutchett Road, Hills Road.
