

Monthly Projects Update – November 2021

Bay Road

- Stormwater works from Coast Rd towards the sea making great progress.
- The contractor, together with Council staff, are working with SA Water where trenching impacts aged SA Water mains. Special consideration is required in crossing each water main, resulting in temporary shut downs whilst the pipe work is laid and backfilled. Residents affected are notified in advance and SA Water are providing alternative water solutions.
- Focus is to complete the entire stage 3 section, including the smaller branches of stormwater and kerbing. This will allow the road construction contractor enough work to mobilise the site and begin the road construction.
- Traffic management and project update notices have been provided to residents along Bay Road and all associated side roads via mail, VMS boards, Council social media platforms and Yorke Peninsula Country Times to the community
- Council is working with SAPN in the installation of electrical conduits for future proofing the undergrounding of powerlines.



Wallaroo to Moonta Shared Path

- Project start-up walkover with the construction crew and site mobilisation has been undertaken.
- Construction team has begun on Coota Road, clearing shrubs and widening the existing trail as they head south toward Moonta.

Sir Richard Williams Statue

- Council working with contractor have installed the concrete slab, memorial rock and granite bench for the installation of the statue.
- In the area surrounding, the memorial site has had roll out lawn placed in readiness for the opening ceremony on 7th November 2021.

Monthly Projects Update – November 2021

North Beach Foreshore Toilet

- Externally, the blue board has been rendered and timber cladding installed.
- Internally, the walls are being lined and nearing completion.
- Final painting will proceed these works as will the plumbing and electrical fit-out that complete the construction works.
- Concrete paths and fencing are scheduled for November to finalise the project.



North Beach Sand Works


- Restoration works on the fore dune system, which will continue to provide protection against sand drift and coastal erosion, commenced on the 12th October 2021.
- These works included mechanically building up the dune to the remaining fence line and building the dunes where the fences have been washed out.
- Mechanical restoration of the dunes removes the need to repair and remove damaged fences and fast-tracks the provision of protection to properties behind the dunes.
- The sand has been harvested from the beach, particularly from along the marina wall where it has built up.
- Deposited seaweed has been combined with the sand to improve the sand's consistency.
- Once completed, the dune is to be capped with additional seaweed to improve moisture holding capacity for planting in 2022.
- Students from Kadina Memorial School interested in Coastal Management will assist in dune levelling in the next week and planting in 2022.



Monthly Projects Update – November 2021

Cemetery Walls - Moonta

- Recent fine weather has assisted in repairing the breach on the Southern wall.
- Works will then commence on the Northern wall.
- A large section of wall affected by a falling tree branch many years ago has been removed and re-laid.

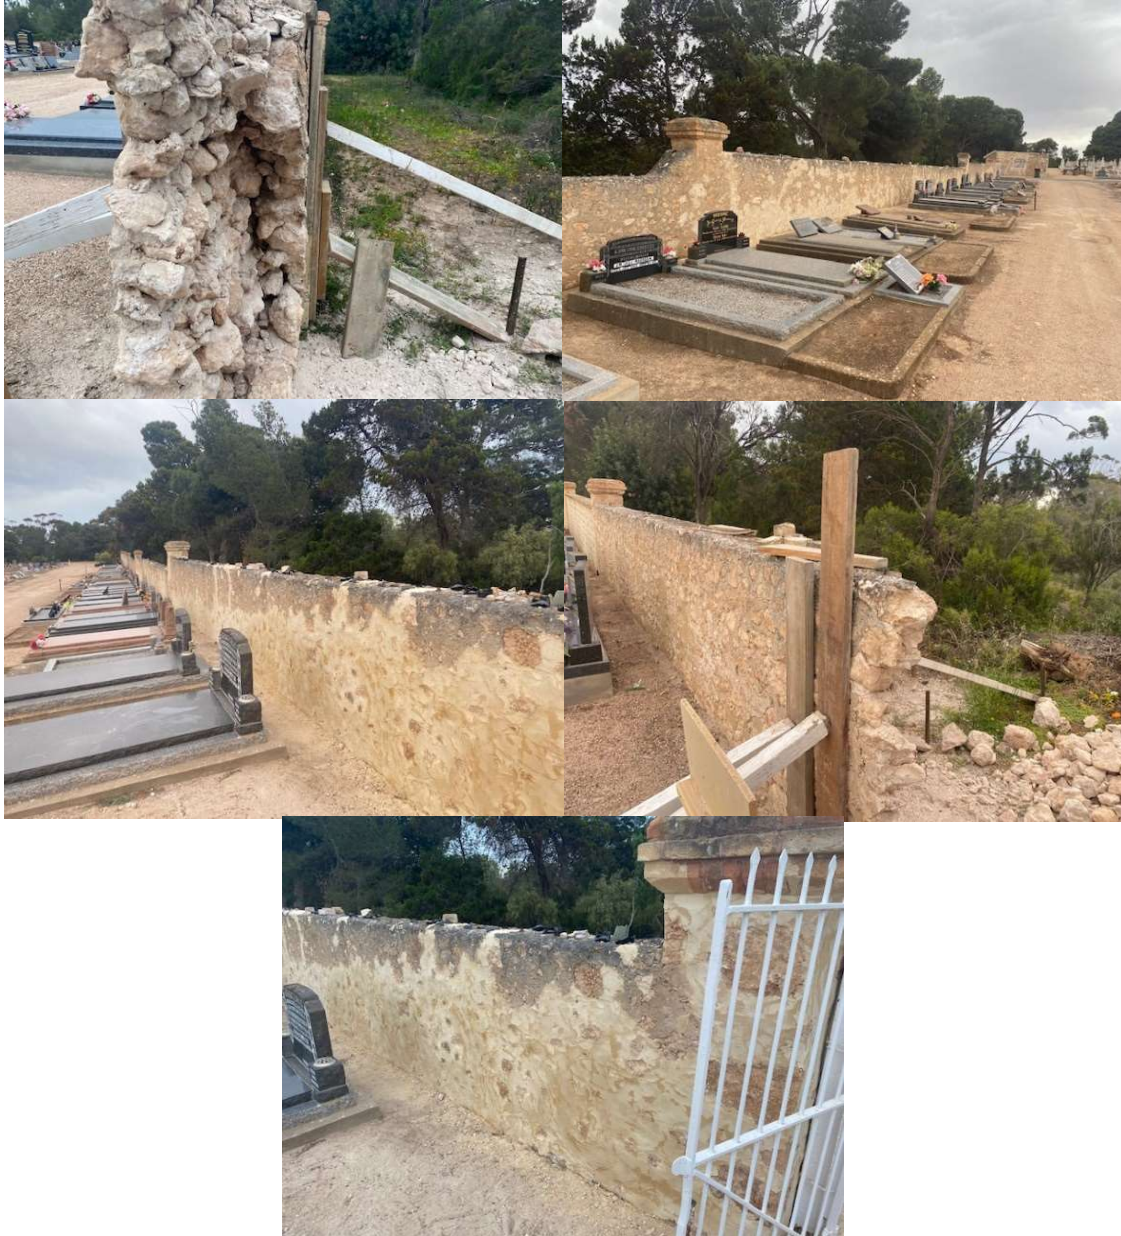

Monthly Projects Update – November 2021

John Terrace - Wallaroo

- Paths and retaining wall are completed.
- Irrigation and reseeding of lawn completed.
- Garden bed planted and mulched.
- Awaiting relocation of power for installation of BBQ, followed by installation of the table and seats.



Unsealed Roads - Patrol Grading

New Holland Road, Sixth Street, Fifth Street, School Terrace, Stoney Ridge Road, Railway Terrace, Drewett Road, West Ella Road, Black Oak Road, Myponie Point Road, Green Plains Road, Rodda Road, Stenning Road, Busshenschutt Road, Copper Hill Road, Pontifex Road, Harrop Road, Holman Road, Paskeville Road, Second Street, Bowey Road, Kainton Road, Point Riley Road, Rosslyn Road, Copper Hill Road, Mitchell Road, Daddow Road.
