

Monthly Projects Update – August 2020

Moonta Town Hall

- Head contractor has been liaising with sub-contractors regarding the additional scope of works
- Now required to manage the budget and not incur a variation.
- Ornate ceiling components are in fabrication and delivery of the first batch is on site.
- Materials for the roof and trusses have been ordered and will be on site in the coming weeks.
- Some additional demolition and asbestos removal has occurred in the cinema area where the
- Extent of works was extended further.
- Month of August is scheduled for the replacement of truss works, only hold point here will be
- Any inclement weather.

Kadina Lagoons


- The anchor trenches for the lagoon liners have been backfilled and access roads around the lagoons are now completed.
- Lagoon 4 and 5 have been lined, tested and certified as per EPA requirements. Lagoons are online and currently filling.
- 3600 tonne of limestone reuse material has been crushed to date.
- Pump station has been installed and is programmed to be commissioned at the end of August.

Timaru Park/Clayton Drive

- Timaru Park lawn has sprouted, but growing slowly due to the cold weather.
- The North Beach Progress Association is currently building the new seating and table for under the BBQ shelter.
- Clayton Drive mural has progressed.

Frances Terrace Road Reconstruction

- SA Water mains upgrade from George Street to Milne Terrace is complete.
- Road reconstruction project has commenced with works including:-
 - Installation of underground electrical conduits in stages 1&2
 - Storm water installation in stage 2
 - Excavation and preparation of kerbing in stages 1 and 2
- Frances Terrace project is divided into 5 stages, image below:

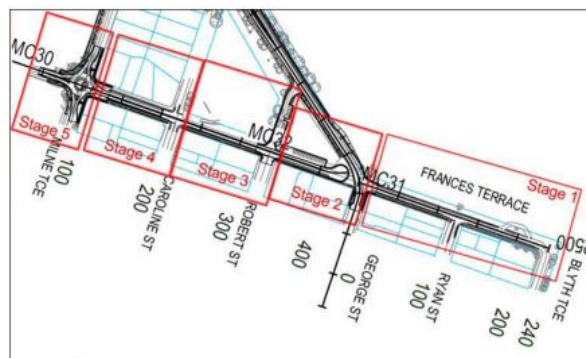

- Project has been staged to limit the inconvenience of road closures.

Monthly Projects Update – August 2020

Johnson Cove Access Ramp

- Stainless steel wire balustrade installation is complete.
- Access Ramp is open to public.
- A meeting with Friends of Port Hughes to be organised in August, with the intent to work with them regarding the revegetating the area around the ramp.



Victoria Square

- Pathway has been sealed in a protective coating.
- Fences and bunting have been removed to allow access through the path.
- Fencing remains around the garden beds that are to have raised concrete borders.
- Concreting scheduled for early August.



Monthly Projects Update – August 2020

Kadina Dog Park

- Landscaping works complete
- Dog agility and exercise equipment installed
- Drinking fountain tap and dog bowl installed
- Rotary shelter installation works ongoing
- Kadina Dog Park is open to the public with Rotary shelter section bunted off.



Kadina Cemetery Walls

- Works are progressing on the entrance wall
- There is considerable damage in these walls, slowing the average completion rate per panel.
- Council staff have been cleaning up and removing unwanted vegetation from the inside of the fence line, which will allow a clean area to revegetate in a consistent or themed species.

North Beach Sand Drift Management Plan

- Stage one of fencing has all been installed, with Stage two dune fencing to be completed once the dune structure has been formed.
- Sand and seaweed harvesting has now ceased with backfilling of the fences and clearing around the homeowners properties complete.
- Stage one of revegetation is complete, with approximately 3,500 plants.
- Council staff are undertaking the irrigation of these plants until established or until a permanent irrigation can be costed and installed.
- Additional fencing to the front of the property owners' homes has been installed to delineate pedestrian movement and safeguard the revegetated areas.
- Consultants are to return in 3 weeks to monitor the sand movement.

Monthly Projects Update – August 2020

Resource Recovery Centre - Weighbridge

- Resource Recovery Centre weighbridge structure installation and concrete deck complete.
- Concrete works have extended to the on and off ramp, service paths and office building.
- Office building has been delivered and installed.
- Electrical and IT service connections to the office building are ongoing to complete the project.
- Wallaroo transfer station weighbridge is scheduled to be opened to the public 3 August 2020.



Splash Town Water Park


- Contractors have now installed the shade sails, which has now completed this project.



Monthly Projects Update – August 2020


Lyndon Avenue, Moonta Bay

- The road was damaged due to recent water main break.
- Minor civil works were undertaken from 3 August 2020 to repair approximately 175m² of road, 50m of kerb, 25m of concrete footpath length and 25m² of concrete driveway
- The sealing of the road has been postponed due to rain, but is set to be complete by 19 August 2020.

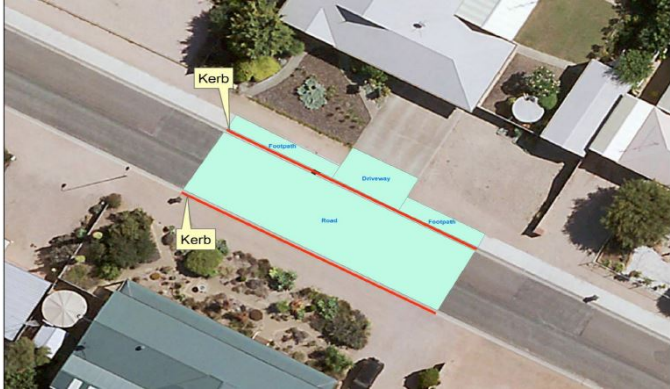

David Street, Kadina

- Project set to commence this month to turn the unsealed David Street (dirt road) into a sealed road with a kerb, path and swale drain for storm water

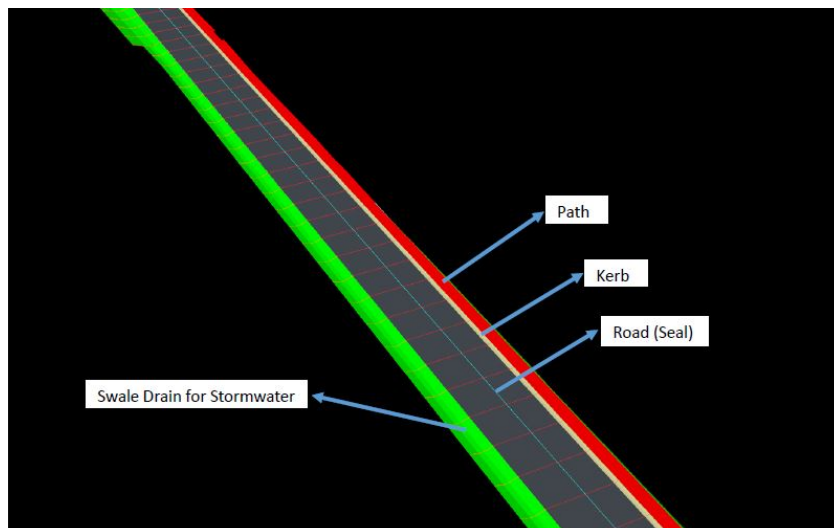

Monthly Projects Update – August 2020

Unsealed Roads

Rees Road, Black Rock Road, Morphett Road, Cross Road, Kinnear Road, Pt Riley Road, Wallaroo-Tickera Road, Chatties Lane, Hopgood Road, Kadina-Tickera Road, Adams Plain Road, Blackoak Road, Beare Road, Leavre Road, Larwood Road, Pine Forrest Road, Willamulka Road, Old Well Road, Thrington Hill Road, Wintinerta Road, Thomas Plain Road, McKay Road, Haynes Road, Retallick Road, Tank Road, Skinner Road, Old Wallaroo Road, Moonta-Cunliffe Road, Sandercock Road, Cavanagh Road, Ryan Road, Crutchett Road, Mill Road, Allen Road, Warmington Road, Rosewarne Road, Martin Terrace, Paskeville Road, West Ella Road, Stoney Ridge Road, Pontifex Road, Harrop Road, Drewett Road, Bowey Road, Bussy Road, Sterle Road.
